

# MCA e-News

Municipal Corporation, Amritsar

AMRITSAR



2019

# MCA e-News

## Clean City Green City



***Green cities have clean air and water and pleasant streets and parks. Green cities are resilient in the face of natural disasters and the risk of major infectious disease outbreaks in such cities is low. Green cities also encourage green behaviour, such as the use of public transit, and their ecological impact are relatively small.***

# Municipal Corporation, Amritsar



# "Heritage Building" And Old Office

Municipal Corporation  
Amritsar





**Sh. Karamjit Singh,  
Hon'ble Mayor,  
Municipal Corporation, Amritsar.**



**Sh. Harbir Singh, I.A.S,  
Commissioner,  
Municipal Corporation, Amritsar.**

***Releasing of monthly E-newsletter is an Endeavour of the Municipal Corporation, Amritsar to make the people of Amritsar City aware about the activities being undertaken by it. It will increase their familiarity with the administration of the Municipal Corporation, Amritsar.***

## **MUNICIPAL CORPORATION AMRITSAR**

### **AMRITSAR SMART CITY :-**

Amritsar Smart City Ltd. is soon coming up with a number of projects which will change the look of the city and provide a feel of the developed and progressive Amritsar.

#### **Development of Spaces below Flyovers in Amritsar - Thematic Lighting and Beautifications**

The proposal intends to beautify the area below the elevated Corridor between Bhandari Bridge to Taranwala Pul on GT Road, and the area below the Kichlu Chowk Flyover. This project will transform these dull and dirty spaces into vibrant, active and safe spaces. The illuminations at night will light the areas below the flyover. The once dark and unsafe area will be hereby transformed into green, active and vibrant space through Thematic LED Lighting. Additionally, seating spaces for the public during afternoon and evening, organized hawking vending spaces with landscape will result in positive usage of the spaces.

The total cost of the project is around 8.34 Crore. Tender to publish soon

#### **Strengthening of underground wastewater services in ABD area**

The current project has been formulated to connect all the households to the underground sewer so that road side drains only carry the storm water during the rains; while in dry season, these drains are dry in walled city.

The total cost of the project is Rs. 13 Cr. approx. Tender published.

#### **Development of Foot Over bridges on BRTS Corridor**

To provide seamless connectivity for pedestrians, multiple locations across the city have been identified for construction of grade separated pedestrian crossings. Amritsar Smart City Limited is developing 2FOBs from the list of 13 shortlisted locations; 1) Outside Shri Guru Harkrishan Public School on G.T. Road and 2) Near Parkash Hospital, Putligarh (GT Road).

### Salient Features of Proposed FOBs

- 2 Lifts (on either side)
- 2 Escalators (Only Ascending Direction)
- And a 5m wide pedestrian Walkway

The total cost of the project is Rs. 5.33 Cr. Tenders shall be floated shortly.

### Smart Road

Main objective of “Smart Road” in Amritsar city is to improve the road condition, traffic congestion, street vendors and illegal on-street parking issues. The 7.4 km Outer Circular Road connecting all the gates of the Walled City of Amritsar has been selected for redevelopment as a smart road. By taking into account the aesthetics of the selected corridor by maintaining the heritage look of the city.

- Development and strengthening of carriage way with uniform lane widths and geometric designs of roads and junctions as per street design standards.
- Development of footpath and NMT track - with uniform widths, non-motorized friendly ways.
- Construction of utility ducts, power lines and optical fiber cables (OFC) and storm riders, – with suitable provision for O&M.
- Construction bus bays, auto bays and on-street parking wherever essential.

Project Cost - The proposed cost for this Detailed Project Report is INR 133 Cr. (inclusive of all taxes). Tender has been floated

### Public Wi-Fi implementation in Heritage Walk area of Golden Temple

The Heritage streetenroute to Golden Temple shall now have high speed free wireless internet facility where users will be able to easily stream a high definition video and browse Internet.

The free high-speed Wi-Fi shall be provided along the 800m stretch from the Partition Museum up to Golden Temple Complex entrance.



ASCL has finalized Sky-Ama Infra Pvt Ltd - Netplus Broadband Services through

an open and competitive Tendering process who shall install Wi-Fi along this stretch within next 3 months.

### **Development of Parks & Open Spaces**

17 Parks and Open Spaces are identified within the city in total, out of which few of the parks are functional and maintained and are in active use. All the parks will be developed around the theme of making them people friendly and accessible with play zones and gyms.

The development of Parks and Open Spaces will have a positive impact on the community around and will hereby contribute to their health and well-being in future.



The total cost of the project is Rs.3.70 Cr.

LED Street light and Installation of Solar Rooftop at 17 No. of Government Building.

## PUNJAB URBAN DEVELOPMENT MISSION

For the 100% development of Amritsar city under the urban mission (west, center, and south) total no. works allotted under urban mission are 156 amounting to Rs.194.73 cr. out of which 156 no. of works has been completed.

## GAS PIPE LINE PROJECT

GAS PIPELINE PROGRESS REPORT						
	Date : 31-May-19					
Sr. No.	Permission details	Project/Area	Permission Length (In Meter)	Length of pipeline laid (In Meter)	Remark	Plan from 01/06/2019 to 30/06/19
1	E.E.-IV/181 dated 18/10/16	From canal bridge to Step N See Shop on Sultanwind Road	1000	1000	All work completed against permission issued. Work completion certificate submitted to MCA.	
2	E.E.-IV/244dated 29/12/16	From Step N See Shop to 4S Chowk (via Sultanwind road to Sherawala Chowk to Ghee Mandi to Hussainpura Bridge to 4S Chowk)	3700	3700	All work completed against permission issued. Work completion certificate submitted to MCA.	

3	No.C/E.E.-4 (Civil)/792 dated 24/08/18	Sultanwind Gate to Golden Temple (Via Mahna Singh Road)	755	740	<p>* All Pipeline laying and testing till the Langar Hall kitchen (Dal making unit) is completed. Now further work for final connectivity shall be undertaken after receiving clearance from SGPC.* DRS (Domestic Regulating station) is need to be set up for further pressure reduction up to required pressure at Langar kitchen. The location and requirement of the land is communicated to SGPC in our meeting dated 04/02/19. But SGPC has not provided clearance for the setting up DRS stating that this matter will be discussed in their committee and after necessary approval permission shall be granted. Hence final pipeline connectivity up to DRS will be planned after receiving permission from SGPC.* Overall work was stopped due to various reasons as mentioned below for <u>32 days</u> 1. Work was stopped by SGPC for total <u>23 days</u> between 13 October 2018 to 29 October 2018 and 19 November to 26 November 2018 on due to Gurupurav festival and Guru Nanak Jayanti. 2. Work was stopped by Local Hoteliers for <u>02 days</u> on 31/12/2018 and 01/01/2019 on the new year eve.3. Work was stopped due to rain for <u>4 days</u> from 19/01/19 to 22/01/194. Work was stopped due to rain on 14/02/19 and 15/01/19* Work progress is slow on account of limited working hours in night i.e. from 11</p>	<p>* Final connectivity till the point where DPRC and MRS is proposed to be installed.</p>
---	--	--	-----	-----	---	--

					pm to 5 am in the morning. Further to that as per the instruction of SGPC work is only allowed on Monday, Tuesday , Wednesday and Thursday due to heavy tourist rush on weekend.	
4	No. C/E.E.-4 (Civil)/792 dated 24/08/18	Chatiwind Gate crossing to Golden temple (Via Ramsar Road)	1273	63	Tap off from 12" main for the pipeline on walled city	
5	No. C/E.E.-4 (Civil)/792 dated 24/08/18	Sultanwind gate crossing to Chatiwind gate crossing (up to Ramsar road)	930	0	As per instruction of MCA, work to be started only after completion of Sultanwind Gate to Golden Temple stretch	NIL
6	No. C/E.E.-4 (Civil)/792 dated 24/08/18	4S Chowk to Cantonment Chowk (Via outer Circular Road, Court Road)	5175	5025	* TOTAL <u>2.1 KM</u> PIPELINE FROM 4S CHOWK TO TRILLIUM MALL HAS BEEN LAID AND <u>COMMISSIONED</u> . WORK COMPLETION CERTIFICATE FOR THE SAME HAS BEEN SUBMITTED TO MCA.* Progress is slow on this stretch on account of traffic, establishments like Hospitals, residents and commercial establishments on the road and unknown utilities like PVC water pipe connections.* Overall work was stopped for <u>28 days</u> due to following reasons:1. From 29/09/2018 to 05/10/2018: on account of heavy rain fall and diversion of the traffic due to cave in on Mall road2. From 05/11/2018 to 12/11/2018 : Festival season and heavy traffic rush on the road3. From 23/11/18 to 25/11/2018: To minimize public in convience on occasion of Gurunanak Jayanti 4. From 19/01/2019 to 22/01/2019	* Complete laying up to Cantonment Chowk (i.e. 2.3 km)* Install 8" isolation valve on the network* Complete installation of DRS* Complete the cleaning, Hydro testing, Swabbing and Drying of the pipeline

					: On account of heavy rains5. From 14/02/2019 to 15/02/2019 : On account of heavy rains6. From 17/05/2019 to 20/05/2019: Work was stopped on instruction of MCA due to General Election7. From 23/05/2019 to 24/05/2019 : Work was stopped on instruction of MCA due to vote counting of Lok Sabha Elections	
7	No. C/E.E.-4 (Civil)/142 dated 19/11/2018	From Nari Niketan to postmortem building of GND hospital on Majitha road	850	850	All work completed against permission issued.	Work completion certificate for issuing NOC to be submitted.
8	No. C/E.E.-4 (Civil)/142 dated 19/11/2018	From Crystal Chowk to Harsha Petrol pump, M.M.Malviya road	80	0	No work started on MM Malviya Road. Permission on Crystal Chowk to Hukamsingh Road for 400 meters length is awaited from MCA.	Complete the laying after receiving permission.
		<b>Total</b>	<b>13763</b>	<b>11378</b>		

## **HRIDAY SCHEME**

### **1. Comprehensive road development and Up-gradation of major roads leading to the Golden Temple (Zone 1)**

Around 14 numbers of roads have been identified under HRIDAY in the Walled City. The length of each road varies from 217m to 1780m. The Rows of all roads also differ in range from 3.86m to 15.68m

**The objective of this project is as follows:-**

- Road lightning is facilitated with architectural shape.
- Roads are strengthened with colour and texture for beautification.

- Roads are paved with different texture, shape and colour to segregate the pedestrian, cycle track and motor vehicle.
- Drains are converted into saucer drain on either side to increase the width of road and to avoid the stringent smell.
- Dustbins are placed at the available corners of roads.
- Provisions of signage are made at important junctions and nodes.

#### Present Status:

- 7 roads have been partially completed out of 14 roads.
- Storm sewer cleaning has been done on Hakima Gate road.
- Facade documentation work has been started on the Katra Ahluwalia Road.

Progress of work:- 100%



## 2. Re-organizing connectivity and Linkages through Roadscape and Landscape improvement at Goal Bagh ( Zone No.3)

The estimated cost of the project is Rs. 5 Crores

The focus of the DPR within the garden is on improving the underdeveloped areas of the site and providing visitor amenities and shaded areas as visitor resting spaces/pause points. The detailed works being undertaken are:

- Landscaping and Horticulture works within the garden
- Provision of cycle track, jogging track and features for universal accessibility.
- Visitor amenities, such as toilets and street lighting;
- Creation of spaces for congregation, pavilions ;
- Street Furniture, including benches and dustbins;
- Open Gym for public.

### Present Status

- Jogging track construction is under way;
- New toilet set purposed is also in progress;
- Repair of boundary wall has also started;
- Steps in front of park are completed.

**Progress of work: 100%**





### 3. Revitalization and infrastructure development at 40 Khoo or 40 Wells of Colonial period (Zone No.5)

**Estimated cost of the project Rs. 5.00 Crores.**

#### SCOPE OF WORK:

- Addressing security and demarcation of edges through a boundary wall;
- Conservation of the 40 wells and colonial period power house;
- Landscaping and Horticulture works within the garden;
- Provision of cycle tracks and features for universal accessibility;
- Small parking and plaza housing visitor amenities, such as toilets and space for vending;
- Provision of focus lighting on the wells and the historic structures;
- Creation of spaces for congregation, OAT, pavilions ;
- Street Furniture;
- Features demonstrating an environmental consciousness, including bio digesters, rain water harvesting chambers etc;
- Interpretation strategy for power house, including signage.





### **Present Status**

- Footpath has been completed;
- Colonial pump house repair and conservation work is underway;
- Boundary wall has been completed upto 800 metres;
- Conservation of wells is also in progress.

Progress of work: 100%

#### **4. Comprehensive improvement of a mobility corridor along the outer and inner circular road (Zone No.4)**

**The cost of this project is Rs. 5 Crores**

Scope of work:-

- Creation of a pedestrian friendly environment through table top crossings, ramps, bollards, shaded pathways (via tree planting), signage etc. to improve Interface between Goal Bagh and surroundings.
- Provision of pedestrian walkways along the inner circular road to create pedestrian friendly environment including provision of space for cycling;
- Restructuring the road to enable corridors for public transport;
- Street furniture and signage near all crossings (developed as pedestrian nodes in the mobility corridor);

- Rotary redevelopment of Hall Gate including surface treatments differentiated by colour and texture, refuge island, bollards, reflective paint, table top crossings, plantation, water features and public art with a unique illumination scheme on signage.
- Provision of Public Art at important junctions and across reclaimed public spaces towards creating a sense of inclusiveness.



### Present Status

- Mastic asphalt has been laid on three rotaries Rambagh Gate, Lohgarh Gate, Hathi Gate;
- Hathi Gate rotary has been reduced in diameter;
- Table top crossings have been done on Lohgarh Gate, Hathi Gate.

Progress of work:           **100%**

## 5. Development of an Environmental park at the UBD Canal for Amritsar (Zone No.5)

Estimated cost is Rs. 1.00 Crores

### Scope of work:-

- Environmental up-gradation of the park;
- Landscape development and provision of signage;
- Revitalize and conserve colonial period Power-House and historic machinery;
- Creation of spaces for congregation, OAT, pavilions.



### **Present Status**

- NOC from the forest department is pending.

Progress of work: 75%

## 6. Structural retrofitting and Up-gradation of the historic fabric of the colonial period building of the Deputy Commissioner of Amritsar's office.

The estimated cost of this project is Rs. 2.00 Crores

## SCOPE OF WORK:

- Structural retrofitting of the DC 's office;
- Creation of improved spaces for public who come to the DC's office and lack visitor facilities and amenities, including creation of plaza with areas for seating, landscaping (softscape and hardscape);
- Provision of visitor amenities, such as toilets, cafeterias for improved public use of the visitors to the building.



### Present Status


- Electrical fittings have been removed from the building.
- Dismantling of mortar from the walls is underway.
- Floor work is also in progress.

**Progress of work: 80%**

**7. Name of work: - Up-gradation of the Maharaja Ranjit Singh Panorama (Zone No.2)**

The estimated cost of this project is 50 lacs

<ul style="list-style-type: none"> <li>• <b>Scope of work</b></li> </ul>
<ul style="list-style-type: none"> <li>• Deep tube-well</li> </ul>
<ul style="list-style-type: none"> <li>• Repair of AC plant</li> </ul>
<ul style="list-style-type: none"> <li>• Repair and painting of the Building</li> </ul>
<ul style="list-style-type: none"> <li>• Replacing of wall papers in Halls 1,2 &amp;3</li> </ul>
<ul style="list-style-type: none"> <li>• Replacing of mats with tiles in Halls 1,2 &amp;3</li> </ul>
<ul style="list-style-type: none"> <li>• Sprinklers/hydrants</li> </ul>
<ul style="list-style-type: none"> <li>• Landscaping at rear side of the Building.</li> </ul>

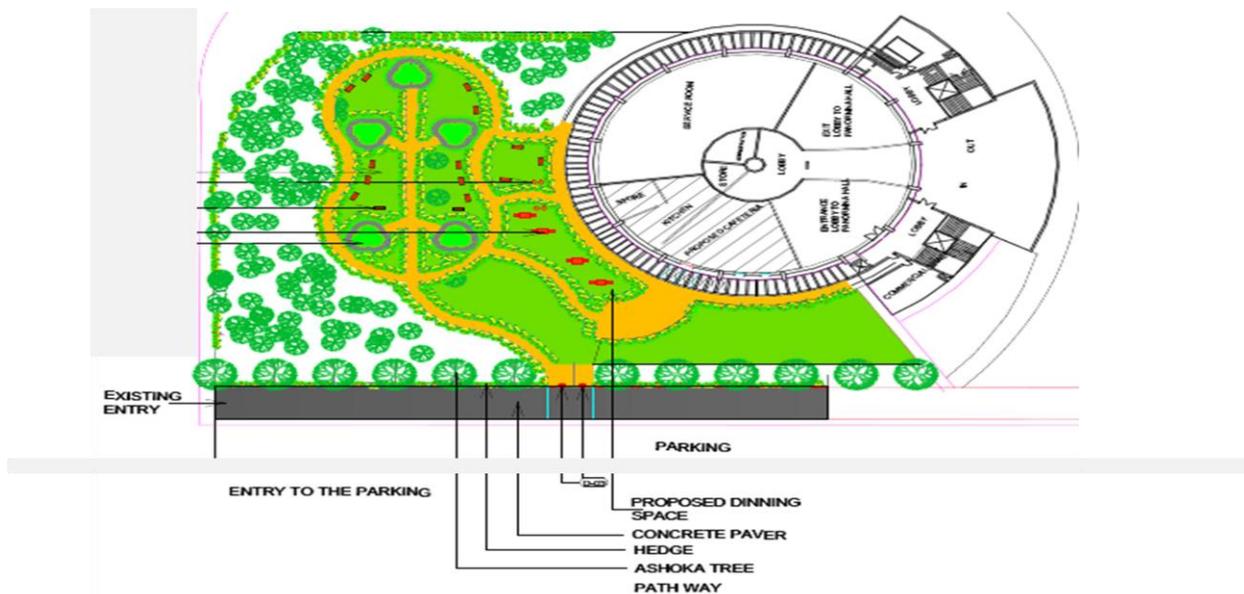

**Present Status**

- The repair work of walls and floor has been completed.
- Painting has been completed
- AC plant repair is in progress.

**Progress of work: 100%**

## 8. Conservation and Revitalization of Ram Bagh Gate

The Total cost is Rs. 1.17 Crore.

### Scope of Work

- Conserve the gate into its original form by use of old traditional materials;
- Development of new care taker room;
- A new rooftop Cafeteria.



### Present Status

- Half of roof has been dismantled and remade;
- Caretaker room is in progress;
- Conservation of the building is also in progress.

**Progress of work: 100%**

## **OPERATION & MAINTENANCE CELL**

1. Under JICA (Japan International Cooperation Agency) assisted Amritsar Sewerage Project amounting to Rs. 600.60 Cr., the work for the construction of Interceptor/Trunk and lateral sewer in South & North Zone is in progress. In South zone area against the scope of work for laying lateral sewer 121.71 Km., Trunk sewer(RCC NP3) 26.96 Km., CIS/RCC HDPE 6.34 Km & house connection 17500 nos. In the South Zone, ***Approx. 114.00 Km. lateral sewer, 25.61 Km. Trunk sewer (RCC NP3), CIS/RCC HDPE 6.34 Km. and 13550 nos. houses are connected with the sewer.*** Similarly in North zone area against the scope of work for laying lateral sewer 270.02 Km., Trunk sewer(RCC NP3) 22.53 Km., Cast in situ 16.66 Km. and house connection 27500 nos. In the North, ***Approx. 147.71 Km. lateral sewer, 26.11 Km. Trunk sewer(RCC NP3),7.98 Km. Cast in situ(km), (M/s. OCR Progress 01 to 06 work) – 136.09 and 2486 nos.+13633 (OCR) houses are connected with the sewer.***

### **Physical Status of STP situated in North Zone:-**

***99% of Civil Work completed. Work of Aeration Tank, MPS, Pre-treatment unit, Primary Clarifier, Secondary Clarifier, Sludge Thickener, Primary Sludge Pump, Biological Sludge Pump, Supernatant Sump, Staff Quarters & Security Guard Room is completed. Construction of units such as, Bio Gas Storage Tank, Digester equipment building and finishing work is in progress.***

2. The project amounting to Rs. 202.34 Cr. in South-East zone of Amritsar Sewerage Project with a scope for providing Water Supply, Sewerage, Sewage Treatment Plants, Roads, Street Light, O&M for 10 years has been approved and the funding agency of this project is JNNURM/GoP/ULBs. The work

has been allotted to the M/s. Shapoorji Pallonji & Co. Pvt. Ltd, SP Centre, 41/44, Minoo Desai Marg, Colaba, Mumbai agency for Rs. 183.59 Cr. and the scope of work includes 47 Km. Water Supply line, 4 Nos. T/wells, 4 Nos. OHSRs, 7500 nos. house connection, 107.30 Km. Lateral sewer, 17.50 Km. main sewer, 20000 nos. house connection, 1 No. MPS (90 MLD), 1 No. IPS (15 MLD), 1 No. STPs (27.50 MLD), 173970 Sq.mtr CC. road, 218750 Sq. mtr metalled road and 3520 nos. street light points with O&M for 10 years. ***Presently, 4 Nos. T/wells commissioned, 48.70 Km Water Supply line laid, 4 Nos. OHSR commissioned. 4307 nos. houses connected with water supply line. 93.52 Km Lateral Sewer, 17.96 Km Main Sewer and 11366 houses connected with Sewer line. STP capacity of 27.50 (mld) work is in 94% and MPS (90 mld) work is in 98% progress at site. 1730 nos. Street Light Pole installed and 1611 nos. wall points installed as per the report of Executive Engineer, Punjab Water Supply & Sewerage Board, Amritsar.***

**Ongoing Projects :-**

**AMRUT PROJECT :-**

- (i) Work of Augmentation of water supply pipe line of Amritsar Town under AMRUT Project (Package-I) amounting of Rs. 4869.07 lacs has been issued vide work order No. C/167 dated 22/01/2019 to M/s. R.S. Builders, Amritsar.
- (ii) Work of Tubewells of water supply project at Amritsar Town (Package-II Tubewells) amounting of Rs. 325.68 lacs has been issued vide work order No. C/166 dated 22/01/2019 to M/s. H.R. Enterprises, Amritsar.
- (iii) Work of Augmentation of water supply of Amritsar Town Distt. Amritsar Package-III OHSR under AMRUT Project

amounting of Rs.646.80 lacs. has been issued vide work order No. N/213 dated 06/03/2019 to M/s. Rajan Builders, Patiala.

**Swachh Iconic Places(SIP) :-**

- (i) **Supply, Operation & Comprehensive maintenance (for 3 years) of 01 Nos. Of Vehicle Mounted High Capacity Suction and Jetting Machines with Storm Water Filtration & Recycling System of 8000 ltrs. Capacity in Amritsar Municipal Corporation amounting of Rs. 4.40 Cr. has been issued vide work order No. N/212 dated 06/03/2019 to M/s. Sadhana Enviro Engineering Services, Bangalore.**
- (ii) **Supply Testing, Commissioning and operational zed of 10 No's Reverse Vending Machines for Pet Bottles along with O&M for three years at various locations around Golden Temple in Municipal Corporation Amritsar amounting of Rs. 76,92,520/- has been issued vide work order No. C/163 dated 09/01/2019 to M/s RVM Recycle Pvt. Ltd., New Delhi.**
- (iii) **Supply and Installation of Smart Semi Underground Waster Collection Bins and Fully Underground Bio compactor and Collection and Transportation of MSW from Smart Bins and Compactor to Dumping Site amounting of Rs. 3,29,75,625/- has been issued vide work order No. C/151 dated 12/11/2018 to M/s. Eco Garb, Tamilnadu.**

**HEALTH DEPARTMENT**

In the month of June, 2019 Municipal Corporation, Amritsar has organized Swachhta awareness rally and shramdaan program under the supervision of Ld. Commissioner and Mayor, in collaboration with Hindustan Petroleum Corporation limited. This Swachhta rally was organized under at

various part of the city like Bhagtwala, Ranjeet Avenue, Majitha Road, Golden temple for the purpose to create awareness about source segregation.

Municipal Corporation Amritsar start working as per the direction given by Honorable NGT in the Case O.A. number 606/2018 and started filing daily report and monthly progress report as per the direction. Special drive for the cleaning under the over bridges and flyovers, vacant plots are done on Regular intervals.

Training program was organized for the purpose to train the safai sewaks in regard of safe handling of waste, Health, hygiene and safety, and Source segregation and its benefits, also message conveyed to them to avoid use of plastic polythene and thermocol in daily life. All the employees of M/s Amritsar MSW Limited were trained and aware about the source segregation of the waste and its benefits.



Integration of rag pickers and role of safai sewaks in SS19, intensive drive held in whole city and awareness campaign made in the regard of health safety and food hygiene. A drive is made for "Say no to Plastic" and citizens were

aware about the source segregation and in-situ processing of the waste. Massive challans were done for the plastic bags, and approximately 4250 kg of plastic bags were seized, and 65 challans were done in this regard.

Daily report for the progress of MSW work and door to door collection of the waste from all the wards of the city is also filed on daily basis on the Swachhta Munch as well PMIDC portal, for the purpose of Swachhta Sarvekshan 2019.

Municipal corporation Amritsar approaching door to door for the purpose of source segregation of waste and showing the demonstration of source segregation of waste as well awareness of the citizens for the source segregation of the waste.



Municipal Corporation Amritsar organized a meeting with the senior officers of the M/s Amritsar MSW in regard of finalizing the plan for the establishment of the processing facility and starting the Collection and transportation of waste from inner wall city and meeting was held under the chairmanship of Honorable Mayor and Ld. Commissioner Municipal Corporation Amritsar.

Municipal Corporation Amritsar planning a pilot project for the collection and transportation of the waste and its processing from the inner wall city of the city as per the direction of the Honorable Mayor and Honorable commissioner and work has started on it and MC Amritsar planning to purchase adequate Machineries approximately worth Rs. 5.05 Cr . Review meeting with the senior staffs of the M/s Amritsar MSW Limited was also held, for the progress of establishment of processing facility of waste in Amritsar.

Municipal Corporation Amritsar planning a pilot project for the collection and transportation of the waste and its processing from the inner wall city of the city as per the direction of the Honorable Mayer and Honorable commissioner and work will be started after the election code.

## **LAND DEPARTMENT**

The Land department of Municipal Corporation, Amritsar has constituted two teams under the supervision of inspectors for the removal of temporary encroachments from foot paths and roads. Other than dealing with the complaints received in the department, these teams remove temporary encroachments in the different parts of the city. Removal of encroachments is an ongoing process and is being under taken on daily basis.

Other then this Enforcement Monitoring Committees have been constituted which conduct weekly meetings and are regularly removing permanent encroachments in different parts of the city at regular intervals.

Also, shopkeepers in the markets are being regularly requested through public address systems to keep their merchandise/goods within their

shops/premises and not to display them on roads/footpaths. Other than regular removal of temporary encroachments from roads and footpaths from different parts of the city, major anti encroachments drives were carried out by the sub-enforcement committee's at Kabir Park, Near Amandeep Hospital, Hakima Gate & Batala Road. Also Land Department collected around Rs. 5.17 Lacs against Rent of shops during the month.

**KABIR PARK, NEAR AMANDEEP HOSPITAL, HAKIMA GATE & BATALA ROAD**



## **ADVERTISEMENT DEPARTMENT**

During the month of June, 2019, the Advertisement Department of the Municipal Corporation, Amritsar has collected revenue to the tune of Rs. 51,84,000/- as Advt. tax. During this period, 53 illegal hoardings/boards have been removed and taken into custody by the Municipal Corporation, Amritsar.

## **STREET LIGHT DEPARTMENT**

ਉਪਰੋਕਤ ਵਿਸ਼ੇ ਸਬੰਧੀ ਸਥਾਨਕ ਸਰਕਾਰ ਵਿਭਾਗ ਦੇ ਪੱਤਰ ਪਿੱਠ ਅੰਕਣ 5/111/2016/4884/506-508 ਮਿਤੀ 16-09-2016 ਰਾਹੀਂ ਅੰਮ੍ਰਿਤਸਰ ਸ਼ਹਿਰ ਵਿਚ ਲੱਗੀਆਂ Conventional ਸਟਰੀਟ ਲਾਈਟ ਨੂੰ ਬਦਲ ਕੇ LED Based Energy Efficient ਸਟਰੀਟ ਲਾਈਟਾਂ ਲਗਾਉਣ ਦੇ ਹੁਕਮ ਕੀਤੇ ਗਏ । ਇਸ ਸਬੰਧੀ ਨਗਰ ਨਿਗਮ, ਅੰਮ੍ਰਿਤਸਰ ਵਲੋਂ ਮਿਤੀ 22/09/2016 ਨੂੰ M/S Energy Efficiency Services Limited (EESL), Noida ਨਾਲ ਇਕਰਾਰਨਾਮਾ ਕੀਤਾ ਗਿਆ । ਜਿਸ ਦੇ ਸਨਮੁੱਖ ਮਿਤੀ 30-04-2018 ਤਕ ਅੰਮ੍ਰਿਤਸਰ ਸ਼ਹਿਰ ਵਿਚ ਲਗਭਗ 3782 LED ਲਾਈਟਾਂ ਵੱਖ ਵੱਖ ਮੁੱਖ ਸੜਕਾਂ ਅਤੇ ਹੋਰ ਇਲਾਕਿਆਂ ਵਿਚ ਲਗਾਈਆਂ ਗਈਆਂ ਹਨ। ਨਗਰ ਨਿਗਮ ਵਲੋਂ ਮਤਾ ਪਾਸ ਕੀਤਾ ਗਿਆ ਹੈ ਕਿ LED Street Light Project Smart City Mission ਦੇ ਅਧੀਨ ਤਬਦੀਲ ਕਰ ਦਿੱਤਾ ਜਾਵੇ ਅਤੇ ਸਰਵੇ ਦਾ ਕੰਮ ਚਾਲੂ ਹੈ ।

ਇਥੇ ਇਹ ਦੱਸਣ ਯੋਗ ਹੋਵੇਗਾ ਕਿ ਉਪਰੋਕਤ ਕੰਮ ਤੇ ਇਲਾਵਾ ਆਮ ਪਬਲਿਕ ਦੀਆਂ ਸਹੂਲਤਾਂ ਨੂੰ ਮੁੱਖ ਰੱਖਦੇ ਹੋਏ ਨਗਰ ਨਿਗਮ ਦੇ ਕੰਮ ਨੂੰ ਸਚਾਰੂ ਢੰਗ ਨਾਲ ਚਲਾਉਣ ਲਈ ਵੱਖ ਵੱਖ ਵਾਰਡਾਂ ਦੀ ਸਟਰੀਟ ਲਾਈਟ ਦੇ ਰਖ ਰਖਾਵ ਨਾਲ ਸਬੰਧਤ ਪ੍ਰਾਪਤ ਸ਼ਿਕਾਇਤਾਂ ਦਾ ਨਿਪਟਾਰਾ ਕਰਨ ਹਿੱਤ ਨਗਰ ਨਿਗਮ ਵਲੋਂ ਸਟਰੀਟ ਲਾਈਟ ਦੇ ਸਮਾਨ ਦੀ ਖ਼ੀਦ ਦਾ ਮਤਾ ਪ੍ਰਵਾਨ ਕਰਨ ਉਪਰੰਤ E-Tender ਰਾਹੀਂ ਠੇਕੇਦਾਰ ਨੂੰ ਅਲਾਟ ਕਰ ਦਿੱਤਾ ਗਿਆ ਹੈ ਅਤੇ ਲਗਭਗ 70 % ਸਮਾਨ ਦੀ ਸਪਲਾਈ ਨਗਰ ਨਿਗਮ ਸਟੋਰ ਵਿਚ ਪ੍ਰਾਪਤ ਹੋ ਚੁੱਕੀ ਹੈ ਅਤੇ ਬਾਕੀ ਸਪਲਾਈ ਲੈਣ ਦਾ ਕੰਮ ਚੱਲ ਰਿਹਾ ਹੈ ।

## **AMRUT SCHEME**



**Release of Rs. 21,11,00,000** as Reform incentive to Govt. of Punjab under Atal Mission for Rejuvenation and Urban Transformation for the year 2019-20

The amount is being released as incentive for achievement of Reforms milestone mandated for financial year 2018-19 as per para 4.3 of the Guidelines of Atal Mission for Rejuvenation and Urban Transformation (AMRUT)

**The aforesaid release will be governed in terms of the following conditions:-**

- The incentive fund is an additionally and no matching funds will be required to be given by the State/ULB.
- The State High Power Steering Committee will decide the use of the incentive amount. the incentive award will only be used in Mission cities on admissible components of AMRUT, including new projects. the SHPSC will inform the MOHUA of the use of incentive funds on projects.
- The incentive cannot be used as the State share in project in the AMRUT, but can be used by the ULB's for their project funding.

- Unutilization funds for Reform incentive will be transferred to project fund every year.
- This release will be governed in terms of provisions of GFR 2017
- No utilization certificate is pending in respect of reform incentive.
- The expenditure involved is debitable to the Major Head-3601-Grants-in-aid to State Govts., 06-Centrally Sponsored Schemes, 06.101-Central Assistance share, 24-Urban Rejuvenation Mission-500Habitations (AMRUT) 24.01-Urban Rejuvenation Mission-500 Habitations (AMRUT), 24.01.31-Grants-in-aid-General under Grant .0.56(plan)-Ministry of Urban Development of the year 2019-20
- The amount of Rs.21,11,00,000 will be credited to the State Government's account to RBI as per procedure laid down by Ministry of Finance,Department Expenditure vide POMNo.F-II(45/76/SC)dated 22.02.1977
- This sanction has been entered at Sl.No.20 of the sanctioned Register.
- This issue with the concurrence of the integrated Finance Division Vide e-file No.3114450dated 21.06.2019



**Phone : 0183-2505450**

**Fax : 0183-2502339**

**Email : [cmcasr@punjab.gov.in](mailto:cmcasr@punjab.gov.in)**

**Website : [www.amritsarcorp.com](http://www.amritsarcorp.com)**

**Complaint Cell: 1800 1802 103**
