

MCA e-News

Municipal Corporation, Amritsar

AMRITSAR



2019

MCA e-News

Clean City Green City



Green cities have clean air and water and pleasant streets and parks. Green cities are resilient in the face of natural disasters and the risk of major infectious disease outbreaks in such cities is low. Green cities also encourage green behaviour, such as the use of public transit, and their ecological impact are relatively small.

Municipal Corporation, Amritsar



"Heritage Building" And Old Office

Municipal Corporation
Amritsar





**Sh. Karamjit Singh,
Hon'ble Mayor,
Municipal Corporation, Amritsar.**



**Sh. Harbir Singh, I.A.S,
Commissioner,
Municipal Corporation, Amritsar.**

Releasing of monthly E-newsletter is an Endeavour of the Municipal Corporation, Amritsar to make the people of Amritsar City aware about the activities being undertaken by it. It will increase their familiarity with the administration of the Municipal Corporation, Amritsar.

MUNICIPAL CORPORATION AMRITSAR

AMRITSAR SMART CITY :-

An Ocean of Enthusiasm and Sportsmanship witnessed

ASCL's Mini Marathon acquired Tremendous Response of Public



On 24th February 2019, Amritsar Smart City organized its first mega event 'Amritsar Mini Marathon' in collaboration with MY FM 94.3 and supported by LIC of India.

Amritsar Smart City Ltd. called upon the free spirit of the people of Amritsar to play their positive and constructive role by participating in this 10 km run for the holy city. This got a tremendous response from public. On the day of event people started gathering early in the morning before 5am. About five thousand people especially youngsters from all walks of life from across the state, participated with great spirit of sportsmanship. MP Gurjit Singh Aujla, MLA Sh. Sunil Dutt, Sr. Divisional Manager of LIC of India, S. Harvinder Singh, and CEO, ASCL Ms. Komal Mittal flag-off the race.

The top 3 participants in both categories (Male & Female) awarded with cash prizes of Rs. 11,000/-, 5,100 & 3,100/-. T-Shirts handed out to all registered participants and refreshments at the finish line. Medals awarded to all the participants successfully finishing the marathon.

Especially abled athletes from various institutions of Amritsar under the flagship of Special Olympics Bharat also participated (below 1km run) and grabbed the attention and appreciation from all. They all has honoured with Medals & Track Suits. Stalls from various government departments were placed for public awareness with the message of better health, save girls child etc. Hockey Olympian, Brigadier Harcharan Singh, Arjuna Awardee was the brand ambassador for this event. He has been a great source of inspiration to the citizens of Amritsar and has shown the way towards ensuring active participation in sports and fitness to the people of Amritsar to be smart and responsible citizens.

S. Harvinder Singh, Sr. Divisional Manager of LIC of India has extended his gratitude towards ASCL for providing LIC with the opportunity to join hands for this great initiative.

The success of the event was visible on the faces of winners, participants, organizers and every person present over there.

Amritsar Smart City won the ‘City Investments to Innovate, Integrate and Sustain (CITIIS) Challenge’ award for Mobility Solution



On 26th of February 2019, Second Apex Conference of CEOs of Smart Cities was held at NDMC Convention Center, New Delhi. ASCL had participated in Mobility Solution category with its Project ‘City Investments to Innovate, Integrate and Sustain (CITIIS) Challenge’ launched by the Ministry of Housing and Urban Affairs (MoHUA) and has been awarded a grant of eighty (80) crores for implementation of Development of sustainable and green public transportation in City.

Ms. Komal Mittal, IAS, CEO of ASCL received this award from Sh. HS Puri, Minister of State for Housing and Urban Affairs and Sh. Durga Shankar Mishra, Secretary MoHUA. In this competition, a total of sixty-seven (67) projects were submitted for competition and only thirteen (13) got short-listed under various categories and Amritsar Smart City Ltd. has been bestowed award for Mobility solution.

This winning proposed project will provide an e-mobility experience to all residents and visitors in the holy City of Amritsar. The present modal share for public transport is 1.5% and project aims at increasing it to 20% through simultaneous reduction of private vehicles. Project primarily aims at an overall improvement of air quality of Amritsar by reduction in carbon footprint.

The ASCL project to implement green mobility shall be manifested through 30 Electric buses and about 9000 Electric three-wheelers being introduced in public transportation system to provide feeder service to the BRTS and also to enhance last mile connectivity. The project also includes creation of adequate charging infrastructure across the city which will further incentivize the citizens to shift towards more eco-friendly modes of transportation

Inauguration of first Two Projects of Amritsar Smart City Projects



On 3rd March 2019, two projects of Amritsar Smart City inaugurated by S. Navjot Singh Sidhu, Cabinet Minister of Local Government, Tourism, Cultural and Museums of State of Punjab in a programme held at Municipal Corporation. Ms. Komal Mittal, IAS, CEO of ASCL said that our team is working from last approximately one year to develop more than fifty projects to make the holy city of Amritsar a Smart City under the Smart City Mission an ambitious initiative of Government of India. The purpose of the Smart Cities Mission is to drive economic growth and improve the quality of life of people by enabling local area development and harnessing technology, especially leading to Smart outcomes. The objective of the SPV (Special Purpose Vehicle) ASCL is to promote the establishment and development of city of Amritsar as a Smart City to provide a decent quality of life to its citizens and a clean and sustainable environment by the application of Smart Solutions like e- governance and various citizen centric services.

Now the wait is over and Amritsar will witness the transforming holy city into a smart city.

PUNJAB URBAN DEVELOPMENT MISSION

For the 100% development of Amritsar city under the urban mission (west, center, and south) total no. works allotted under urban mission are 156 amounting to Rs.194.73 cr. out of which 156 no. of works has been completed.

GAS PIPE LINE PROJECT

The status of laying of Gas Pipe Line for City Gas Distribution Network in the jurisdiction of Municipal Corporation, Amritsar, as on 15-2-19 is as below;

Sr. No	Letter No & Date of Permission for Gas Pipe Line	Length	Physical progress	Time taken for completion	Remarks
1	No. E.E.-IV(C)/181 dt.18.10.2016	1000 mtr.	1000 meter	4 months	Final completion report pending from GSPL.
2	No. E.E.-IV(C)/244 dt.29.12.16	3700 mtr	3700 meter	19 months	Final completion report pending from GSPL.
3	No. E.E.-IV(C)/792 dt. 24-8-18	8133 mtr	3173 meter	45 days	Work in progress. Six km Gas Pipe Line still to be laid by GSPL.
4	No.E.E-IV(C)/140 dt. 19-11-18	(-) 930 mtr	NA	NA	Demand notice pending with GSPL.
	Total :	12833 mtr or 12.83 KM	7873 meter or 7.87 KM		

HRIDAY SCHEME

1. Comprehensive road development and Up-gradation of major roads leading to the Golden Temple (Zone 1)

Around 14 numbers of roads have been identified under HRIDAY in the Walled City. The length of each road varies from 217m to 1780m. The Rows of all roads also differ in range from 3.86m to 15.68m


The objective of this project is as follows:-

- Road lightning is facilitated with architectural shape.
- Roads are strengthened with colour and texture for beautification.
- Roads are paved with different texture, shape and colour to segregate the pedestrian, cycle track and motor vehicle.
- Drains are converted into saucer drain on either side to increase the width of road and to avoid the stringent smell.
- Dustbins are placed at the available corners of roads.
- Provisions of signage are made at important junctions and nodes.

Present Status:

- 7 roads have been partially completed out of 14 roads.
- Storm sewer cleaning has been done on Hakima Gate road.
- Facade documentation work has been started on the Katra Ahluwalia Road.

Progress of work:- 95%

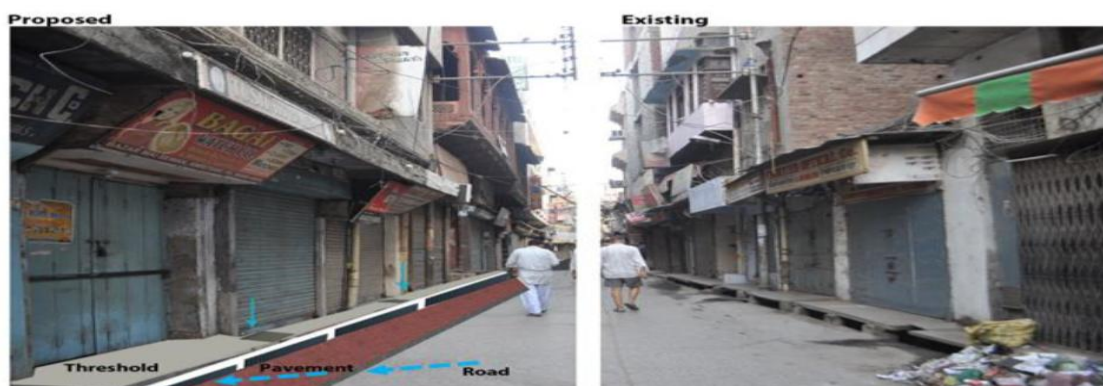



2. Re-organizing connectivity and Linkages through Roadscape and Landscape improvement at Goal Bagh (Zone No.3)

The estimated cost of the project is Rs. 5 Crores

The focus of the DPR within the garden is on improving the underdeveloped areas of the site and providing visitor amenities and shaded areas as visitor resting spaces/pause points. The detailed works being undertaken are:

- Landscaping and Horticulture works within the garden
- Provision of cycle track, jogging track and features for universal accessibility.
- Visitor amenities, such as toilets and street lighting;
- Creation of spaces for congregation, pavilions ;
- Street Furniture, including benches and dustbins;
- Open Gym for public.

Present Status

- Jogging track construction is under way;
- New toilet set purposed is also in progress;
- Repair of boundary wall has also started;
- Steps in front of park are completed.

Progress of work: 100%




3. Revitalization and infrastructure development at 40 Khoo or 40 Wells of Colonial period (Zone No.5)

Estimated cost of the project Rs. 5.00 Crores.

SCOPE OF WORK:

- Addressing security and demarcation of edges through a boundary wall;
- Conservation of the 40 wells and colonial period power house;
- Landscaping and Horticulture works within the garden;
- Provision of cycle tracks and features for universal accessibility;
- Small parking and plaza housing visitor amenities, such as toilets and space for vending;
- Provision of focus lighting on the wells and the historic structures;
- Creation of spaces for congregation, OAT, pavilions ;
- Street Furniture;
- Features demonstrating an environmental consciousness, including bio digesters, rain water harvesting chambers etc;
- Interpretation strategy for power house, including signage.

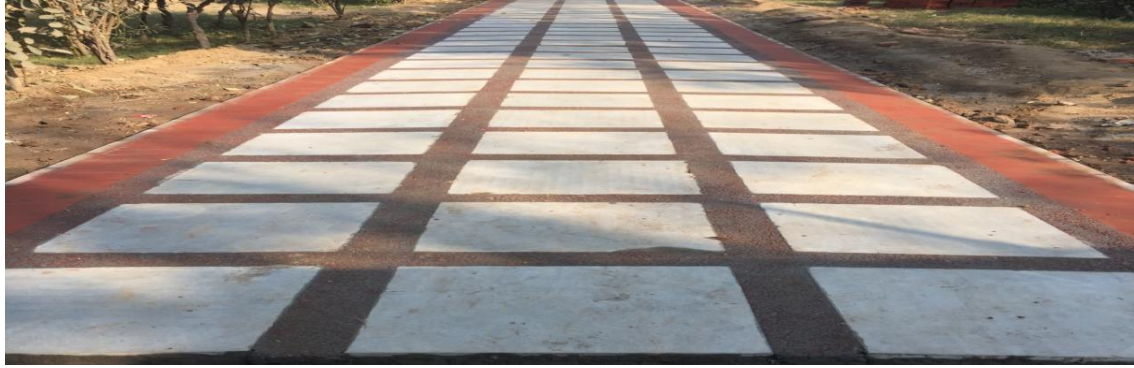

Present Status

- Footpath has been completed;
- Colonial pump house repair and conservation work is underway;
- Boundary wall has been completed upto 800 metres;
- Conservation of wells is also in progress.

Progress of work: 100%

4. Comprehensive improvement of a mobility corridor along the outer and inner circular road (Zone No.4)

The cost of this project is Rs. 5 Crores

Scope of work:-

- Creation of a pedestrian friendly environment through table top crossings, ramps, bollards, shaded pathways (via tree planting), signage etc. to improve Interface between Goal Bagh and surroundings.
- Provision of pedestrian walkways along the inner circular road to create pedestrian friendly environment including provision of space for cycling;
- Restructuring the road to enable corridors for public transport;
- Street furniture and signage near all crossings (developed as pedestrian nodes in the mobility corridor);
- Rotary redevelopment of Hall Gate including surface treatments differentiated by colour and texture, refuge island, bollards, reflective paint, table top crossings, plantation, water features and public art with a unique illumination scheme on signage.
- Provision of Public Art at important junctions and across reclaimed public spaces towards creating a sense of inclusiveness.



Present Status

- Mastic asphalt has been laid on three rotaries Rambagh Gate, Lohgarh Gate, Hathi Gate;
- Hathi Gate rotary has been reduced in diameter;
- Table top crossings have been done on Lohgarh Gate, Hathi Gate.

Progress of work: 99%

5. Development of an Environmental park at the UBD Canal for Amritsar (Zone No.5)

Estimated cost is Rs. 1.00 Crores

Scope of work:-

- Environmental up-gradation of the park;
- Landscape development and provision of signage;
- Revitalize and conserve colonial period Power-House and historic machinery;
- Creation of spaces for congregation, OAT, pavilions.



Present Status

- NOC from the forest department is pending.

Progress of work: 75%

6. Structural retrofitting and Up-gradation of the historic fabric of the colonial period building of the Deputy Commissioner of Amritsar's office.

The estimated cost of this project is Rs. 2.00 Crores

SCOPE OF WORK:

- Structural retrofitting of the DC 's office;
- Creation of improved spaces for public who come to the DC's office and lack visitor facilities and amenities, including creation of plaza with areas for seating, landscaping (softscape and hardscape);
- Provision of visitor amenities, such as toilets, cafeterias for improved public use of the visitors to the building.



Present Status


- Electrical fittings have been removed from the building.
- Dismantling of mortar from the walls is underway.
- Floor work is also in progress.

Progress of work: 75%

7. Name of work: - Up-gradation of the Maharaja Ranjit Singh Panorama (Zone No.2)

The estimated cost of this project is 50 lacs

• Scope of work
• Deep tube-well
• Repair of AC plant
• Repair and painting of the Building
• Replacing of wall papers in Halls 1,2 &3
• Replacing of mats with tiles in Halls 1,2 &3
• Sprinklers/hydrants
• Landscaping at rear side of the Building.

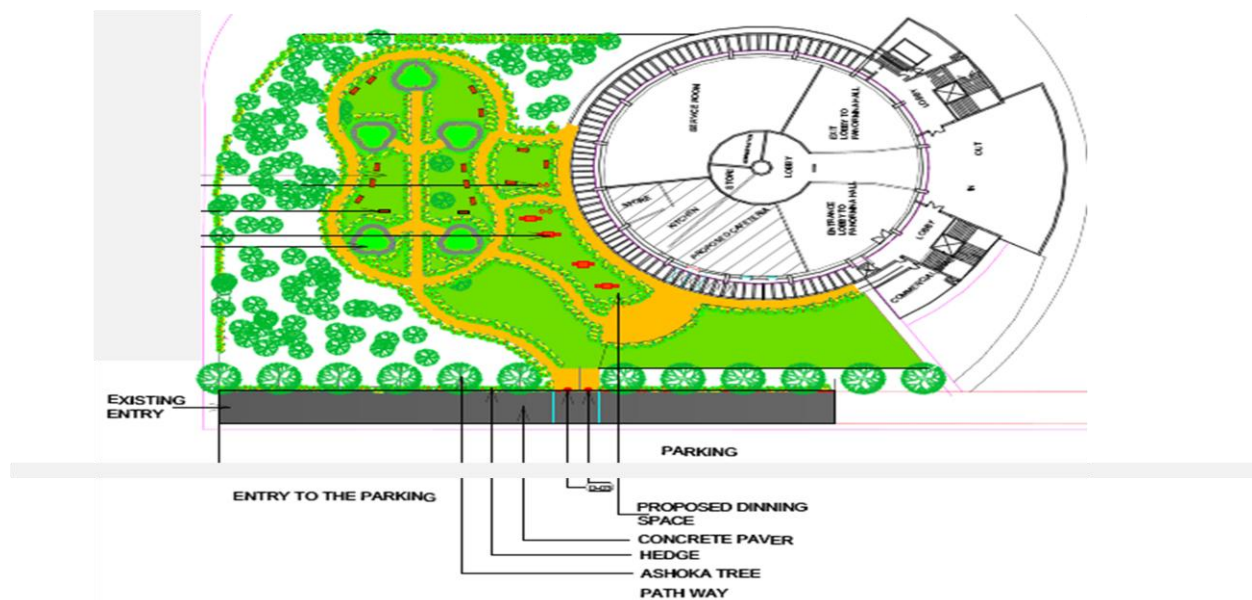

Present Status

- The repair work of walls and floor has been completed.
- Painting has been completed
- AC plant repair is in progress.

Progress of work: 100%

8. Conservation and Revitalization of Ram Bagh Gate

The Total cost is Rs. 1.17 Crore.

Scope of Work

- Conserve the gate into its original form by use of old traditional materials;
- Development of new caretaker room;
- A new rooftop Cafeteria.



Present Status

- Half of roof has been dismantled and remade;
- Caretaker room is in progress;
- Conservation of the building is also in progress.

Progress of work: 100%

OPERATION & MAINTENANCE CELL

1. Under JICA (Japan International Cooperation Agency) assisted Amritsar Sewerage Project amounting to Rs. 600.60 Cr., the work for the construction of Interceptor/Trunk and lateral sewer in South & North Zone is in progress. In South zone area against the scope of work for laying lateral sewer 121.71 Km., Trunk sewer(RCC NP3) 26.96 Km., CIS/RCC HDPE 6.34 Km & house connection 17500 nos. In the South Zone, ***Approx. 114.00 Km. lateral sewer, 25.61 Km. Trunk sewer(RCC NP3), CIS/RCC HDPE 6.34 Km. and 13550 nos. houses are connected with the sewer.*** Similarly in North zone area against the scope of work for laying lateral sewer 270.02 Km., Trunk sewer(RCC NP3) 22.53 Km., Cast in situ 16.66 Km. and house connection 27500 nos. In the North, ***Approx. 147.71 Km. lateral sewer, 26.11 Km. Trunk sewer(RCC NP3),7.98 Km. Cast in situ(km), (M/s. OCR Progress 01 to 06 work) – 136.09 and 2486 nos.+13633 (OCR) houses are connected with the sewer.***

Physical Status of STP situated in North Zone:-

99% of Civil Work completed. Work of Aeration Tank, MPS, Pre-treatment unit, Primary Clarifier, Secondary Clarifier, Sludge Thickener, Primary Sludge Pump, Biological Sludge Pump, Supernatant Sump, Staff Quarters & Security Guard Room is completed. Construction of units such as, Bio Gas Storage Tank, Digester equipment building and finishing work is in progress.

2. The project amounting to Rs. 202.34 Cr. in South-East zone of Amritsar Sewerage Project with a scope for providing Water Supply, Sewerage, Sewage Treatment Plants, Roads, Street Light, O&M for 10 years has been approved and the funding agency of this project is JNNURM/GoP/ULBs. The work has been

allotted to the M/s. Shapoorji Pallonji & Co. Pvt. Ltd, SP Centre,41/44,Minoo Desai Marg,Colaba,Mumbai agency for Rs. 183.59 Cr. and the scope of work includes 47 Km. Water Supply line, 4 Nos. T/wells, 4 Nos. OHSRs, 7500 nos. house connection, 107.30 Km. Lateral sewer,17.50 Km. main sewer,20000 nos. house connection,1 No. MPS (90 MLD), 1 No. IPS (15 MLD),1 No. STPs (27.50 MLD), 173970 Sq.mtr CC. road, 218750 Sq. mtr metalled road and 3520 nos. street light points with O&M for 10 years. ***Presently, 4 Nos. T/wells commissioned,48.02 Km Water Supply line laid,4 Nos. OHSR commissioned. 4051 nos. houses connected with water supply line. 84.93 Km Lateral Sewer,17.81 Km Main Sewer and 6718 houses connected with Sewer line. STP capacity of 27.50 (mld) work is in 81% and MPS(90 mld) work is in 83% progress at site. 1745 nos. Street Light Pole installed and 1733 nos. wall points installed as per the report of Executive Engineer, Punjab Water Supply & Sewerage Board,Amritsar.***

Ongoing Projects :-

AMRUT PROJECT :-

- (i) Work of Augmentation of water supply pipe line of Amritsar Town under AMRUT Project (Package-I) amounting of Rs. 4869.07 lacs. has been issued vide work order No.C/167 dated 22/01/2019 to M/s. R.S. Builders,Amritsar.
- (ii) Work of Tubewells of water supply project at Amritsar Town (Package-II Tubewells) amounting of Rs. 325.68 lacs. has been issued vide work order No.C/166 dated 22/01/2019 to M/s. H.R. Enterprises,Amritsar.
- (iii) Work of Augmentation of water supply of Amritsar Town Distt. Amritsar Package-III OHSR under AMRUT Project

amounting of Rs.646.80 lacs. has been issued vide work order No.N/213 dated 06/03/2019 to M/s. Rajan Builders,Patiala.

Swachh Iconic Places(SIP) :-

- (i) Supply, Operation & Comprehensive maintenance (for 3 years) of 01 Nos. Of Vehicle Mounted High Capacity Suction and Jetting Machines with Storm Water Filtration & Recycling System of 8000 ltrs. Capacity in Amritsar Municipal Corporation. amounting of Rs. 4.40 Cr. has been issued vide work order No.N/212 dated 06/03/2019 to M/s. Sadhana Enviro Engineering Services, Bangalore.
- (ii) Supply Testing, Commissioning and operational zed of 10 No's Reverse Vending Machines for Pet Bottles along with O&M for three years at various locations around Golden Temple in Municipal Corporation Amritsar amounting of Rs. 76,92,520/- has been issued vide work order No.C/163 dated 09/01/2019 to M/s. RVM Recycle Pvt. Ltd., New Delhi.
- (iii) Supply and Installation of Smart Semi Underground Waster Collection Bins and Fully Underground Bio compactor and Collection and Transportation of MSW from Smart Bins and Compactor to Dumping Site amounting of Rs. 3,29,75,625/- has been issued vide work order No.C/151 dated 12/11/2018 to M/s. Eco Garb, Tamilnadu.

- Work of Providing Professional support for engaging out sourced staff for 2 years in Municipal Corporation Amritsar has been issued vide work order No.C/168 dated 28/02/2019 to M/s. Secure Guard Security & Manpower Services, Chandigarh.

JICA assisted Amritsar Sewerage Project (ID-P186): Turnkey Design and Construction of 95 MLD Sewage Treatment Plant, Main Pumping Station at WadalaBhittewad (Near VillageGhausabad) and Intermediate Pumping Stations in North Zone on International Competitive Bidding for JICA-ASP-002

MAIN PUMPING STATION INLET:-



MAIN PUMPING STATION:-



PRE TREATMENT UNIT:-



PRIMARY SEDIMENT TANK:-



AERATION TANK:-



SECONDARY SEDIMENT TANK:-



GRAVITY SLUDGE THICKENER:-



**SUPERNATANT SUMP & THICKENED
SLUDGE TRANSFER PUMP HOUSE:-**



PRIMARY SLUDGE PUMP HOUSE:-



**BIOLOGICAL SLUDGE SUMP &
PUMP HOUSE:-**



AIR BLOWER ROOM:-



CENTRIFUSE BUILDING:-



ANAROBIC SLUDGE DIGESTER:-



DIGESTED EQUIPMENT BUILDING:-



CHIMNEY:-



CHLORINE CONTACT TANK:-



CCT BUILDING:-



BIO-GAS STORAGE TANK:-



STAFF QUARTER:-



ROAD AT SITE:-



HEALTH DEPARTMENT

In the month of February, 2019 Municipal Corporation, Amritsar has organized Swachhta awareness rally and shramdaan program under the supervision of Ld. Commissioner, in collaboration with Hindustan Petroleum Corporation limited. This Swachhta rally was organized under "Swachhta Hi Sewa" near Bhagtwala and near golden temple area and awareness program by Swachhta Rath regarding SBM, SWM and to make city open defecation free was done in various wards of the city.

Citizens were awarded about the importance of the source segregation of the waste, and massive drive organized to control open burning of bio mass as well municipal solid waste, and use of plastic articles.

Training program was organized for the purpose to train the safaisewaks in regard of safe handling of waste, Health, hygiene and safety, and Source segregation and it's benefits, also message conveyed to them to avoid use of plastic polythene and thermocol in daily life, Integration of rag pickers and role of safaisewaks in solid waste management, intensive drive held in whole city and awareness campaign made in the regard of health safety and food hygiene. A drive is made for "Say no to Plastic" and citizens were aware about the source segregation and in-situ processing of the waste in various parts of the city.

Door to door collection of the waste started in the inner wall city of the Amritsar, and whole city will be covered with door to door collection by M/s Amritsar MSW Limited upto 28 February 2019.

Swachhta rally and Swachhta Pakhwara organized by the Municipal Corporation Amritsar, and workers of railway workshop and bus stand were aware about the segregation of waste and use of Swachhta app for the purpose to register their complaints and their feedback about the complaint resolution.

Municipal Corporation Amritsar organized rally, Natak, awareness campaign and painting competition near golden temple and Durgiana temple and three outstanding performing students by the Ld. Commissioner and Joint Commissioner Municipal Corporation Amritsar. During this event citizens were aware about the source segregation 3R principle of waste management and use of Swachhta App.

Honorable Minister Local Government, Honorable Mayor and Ld. Commissioner Municipal Corporation Amritsar putted their vision for bio

remediation of old dumped waste at three dumping sites of the city within 6 to 8 months during a press conference at Bhagtwala, and in this connection meeting was held under the chairmanship of Ld. Commissioner Municipal corporation Amritsar, and it was decided that the concessionaire will install three sets of machines for the purpose of the Bio remediation, at the Bhagtwala and 2 sets of machines at Chabbal road and the concessionaire moved forward at this direction and one set of machine is installed and inaugurated by then honorable Local Government Minister.

LAND DEPARTMENT


The Land department of Municipal Corporation, Amritsar has constituted two teams under the supervision of inspectors for the removal of temporary encroachments from foot paths and roads. Other than dealing with the complaints received in the department, these teams remove temporary encroachments in the different parts of the city. Removal of encroachments is an ongoing process and is being under taken on daily basis.

Other than this Enforcement Monitoring Committees have been constituted which conduct weekly meetings and are regularly removing permanent encroachments in different parts of the city at regular intervals.

Also, shopkeepers in the markets are being regularly requested through public address systems to keep their merchandise/goods within their shops/premises and not to display them on roads/footpaths. Other than regular removal of temporary encroachments from roads and footpaths from different parts of the city, major anti encroachments drives were carried out by the sub-

enforcement committee's at Mahan Singh Gate, Sheran wala Gate, Kesari Bagh, Darbaar Sahib, Sultanwind Road & Tarntaran Road. Also Land Department collected around Rs. 7.20 Lacs against Rent of shops during the month.

**MAHAN SINGH GATE, SHERAN WALA GATE, KESARI BAGH, DARBAAR SAHIB,
SULTANWIND ROAD & TARNTARAN ROAD**

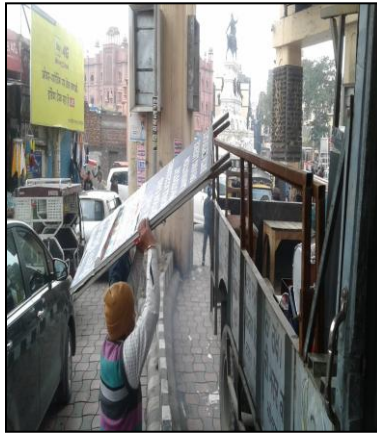

ADVERTISEMENT DEPARTMENT

During the month of February, 2019, the Advertisement Department of the Municipal Corporation, Amritsar has collected revenue to the tune of Rs. 89,700/- as Advt. tax. During this period, 30 illegal hoardings/boards have been removed and taken into custody by the Municipal Corporation, Amritsar.

STREET LIGHT DEPARTMENT

ਉਪਰੋਕਤ ਵਿਸ਼ੇ ਸਬੰਧੀ ਸਥਾਨਕ ਸਰਕਾਰ ਵਿਭਾਗ ਦੇ ਪੱਤਰ ਪਿੱਠ ਅੰਕਣ 5/111/2016/4884/506-508 ਮਿਤੀ 16-09-2016 ਰਾਹੀਂ ਅੰਮ੍ਰਿਤਸਰ ਸ਼ਹਿਰ ਵਿਚ ਲੱਗੀਆਂ Conventional ਸਟਰੀਟ ਲਾਈਟ ਨੂੰ ਬਦਲ ਕੇ LED Based Energy Efficient ਸਟਰੀਟ ਲਾਈਟਾਂ ਲਗਾਉਣ ਦੇ ਹੁਕਮ ਕੀਤੇ ਗਏ । ਇਸ ਸਬੰਧੀ ਨਗਰ ਨਿਗਮ, ਅੰਮ੍ਰਿਤਸਰ ਵਲੋਂ ਮਿਤੀ 22/09/2016 ਨੂੰ M/S Energy Efficiency Services Limited (EESL), Noida ਨਾਲ ਇਕਰਾਰਨਾਮਾ ਕੀਤਾ ਗਿਆ । ਜਿਸ ਦੇ ਸਨਮੁੱਖ ਮਿਤੀ 30-04-2018 ਤਕ ਅੰਮ੍ਰਿਤਸਰ ਸ਼ਹਿਰ ਵਿਚ ਲਗਭਗ 3782 LED ਲਾਈਟਾਂ ਵੱਖ ਵੱਖ ਮੁੱਖ ਸੜਕਾਂ ਅਤੇ ਹੋਰ ਇਲਾਕਿਆਂ ਵਿਚ ਲਗਾਈਆਂ ਗਈਆਂ ਹਨ। ਨਗਰ ਨਿਗਮ ਵਲੋਂ ਮਤਾ ਪਾਸ ਕੀਤਾ ਗਿਆ ਹੈ ਕਿ LED Street Light Project Smart City Mission ਦੇ ਅਧੀਨ ਤਬਦੀਲ ਕਰ ਦਿੱਤਾ ਜਾਵੇ ।

ਇਥੇ ਇਹ ਦੱਸਣ ਯੋਗ ਹੋਵੇਗਾ ਕਿ ਉਪਰੋਕਤ ਕੰਮ ਤੇ ਇਲਾਵਾ ਆਮ ਪਬਲਿਕ ਦੀਆਂ ਸਹੂਲਤਾਂ ਨੂੰ ਮੁੱਖ ਰੱਖਦੇ ਹੋਏ ਨਗਰ ਨਿਗਮ ਦੇ ਕੰਮ ਨੂੰ ਸਚਾਰੂ ਢੰਗ ਨਾਲ ਚਲਾਉਣ ਲਈ ਵੱਖ ਵੱਖ ਵਾਰਡਾਂ ਦੀ ਸਟਰੀਟ ਲਾਈਟ ਦੇ ਰਖ ਰਖਾਵ ਨਾਲ ਸਬੰਧਤ ਪ੍ਰਾਪਤ ਸ਼ਿਕਾਇਤਾਂ ਦਾ ਨਿਪਟਾਰਾ ਕਰਨ ਹਿੱਤ ਨਗਰ ਨਿਗਮ ਵਲੋਂ ਸਟਰੀਟ ਲਾਈਟ ਦੇ ਸਮਾਨ ਦੀ ਖ਼ੀਦ ਦਾ ਮਤਾ ਪ੍ਰਵਾਨ ਕਰਨ ਉਪਰੰਤ E-Tender ਰਾਹੀਂ ਠੇਕੇਦਾਰ ਨੂੰ ਅਲਾਟ ਕਰ ਦਿੱਤਾ ਗਿਆ ਹੈ ਅਤੇ ਲਗਭਗ 65 % ਸਮਾਨ ਦੀ ਸਪਲਾਈ ਨਗਰ ਨਿਗਮ ਸਟੋਰ ਵਿਚ ਪ੍ਰਾਪਤ ਹੋ ਚੁੱਕੀ ਹੈ ਅਤੇ ਬਾਕੀ ਸਪਲਾਈ ਲੈਣ ਦਾ ਕੰਮ ਚੱਲ ਰਿਹਾ ਹੈ ।

AMRUT SCHEME



Reform: Urban Planning and City Development Plan

Milestone: Develop at least one children park in AMRUT city every year

Development/construction and value addition in a park with facilities for children, elderly and differently abled

- Completion certificates of parks developed in 2018-19
- Copies of work order/tender document if it is being developed in 2018-19

Activities/Steps: Completion certificates and photographs of the parks developed in last three years i.e.2015 to 2018

Status: Company bagh Children Park has been developed

Reform: Urban Planning and City Level Plans

Milestone: Preparation of GIS based Master Plans

Base map prepared

Draft master plan is prepared

GIS based Master plan is notified

Activities/Steps: Contract awarded/certification of in-house master plan formulation

- Copy of contract awarded/certificate of in-house master plan formulation
- Certificate of geo-database creation/base map
- Copy of draft master plan

Copy of notified GIS based master plan

Status: Consultants from ISPER had visited Amritsar on 7-9 Jan for data collection. Data has been collected from different departments of Amritsar. Data which is collected has been compiled by the consultants.

Reform: Augmenting Double Entry Accounting

Milestone: Publication of Annual Financial Statement on Website

Activities/Steps: Publication of Audited Annual Financial statements of previous 3 years and financial statement of current FY 2018-19 on website

- Screen shot of Annual statements on-line along with URL

Copies of Annual Financial statements for last 3 years

Status: Annual financial statements up to 2016-17 have been uploaded on website of MCA. Internal Auditor report for the year 2012-13 to 2016-17 have also been uploaded on website of MCA. Further the work is in progress



Phone : 0183-2505450

Fax : 0183-2502339

Email : cmcasr@punjab.gov.in

Website : www.amritsarcorp.com

Complaint Cell: 1800 1802 103
